

ROYAL[®]
aawas

Tirupati | by Royal Group

Construction Update
CLUB HOUSE
December 2024

December 2024



Block - A

Structural Work

- Up to 14th Floor (Terrace) roof slab casted.
- Mumty, OHWT, Pergola casted.

Plastering Work

- Up to 13th Floor internal plaster completed.
- 14th floor internal plaster in progress.
- External Plaster in Progress (40%)

Plumbing Work

- Up to 14th Floor plumbing concealed work completed.

Masonry Work

- Up to 14th Floor AAC Block masonry completed.

Waterproof Work

- Up to 13th Floor down slab waterproofing in Progress

Electrical Work

- Up to 14th Floor electrical pipe concealed work completed.

December 2024



Block - B

Structural Work

- Up to 14th Floor (Terrace) roof slab casted.
- Mumty, OHWT, Pergola casted.

Plastering Work

- 14th Floor internal plaster completed.
- External Plaster in Progress (95%).

Plumbing Work

- Up to 14th Floor plumbing concealed work completed.
- Vertical Sewage, Soil, Rainwater, Kitchen & Balcony outlet & Water line in progress (95%)
- Horizontal Sewage Soil line of Bathroom down slab in progress (90%)

Masonry Work

- Up to 14th Floor AAC Block masonry completed.

Internal Wall Putty Work

- Up to 14th Floor internal wall putty in progress

Waterproof Work

- Up to 14th Floor down slab waterproofing in progress.


Tiles Work

- 3rd and 4th Floor, floor tiles fitting in progress.

Electrical Work

- Up to 14th Floor electrical pipe concealed work completed.

December 2024

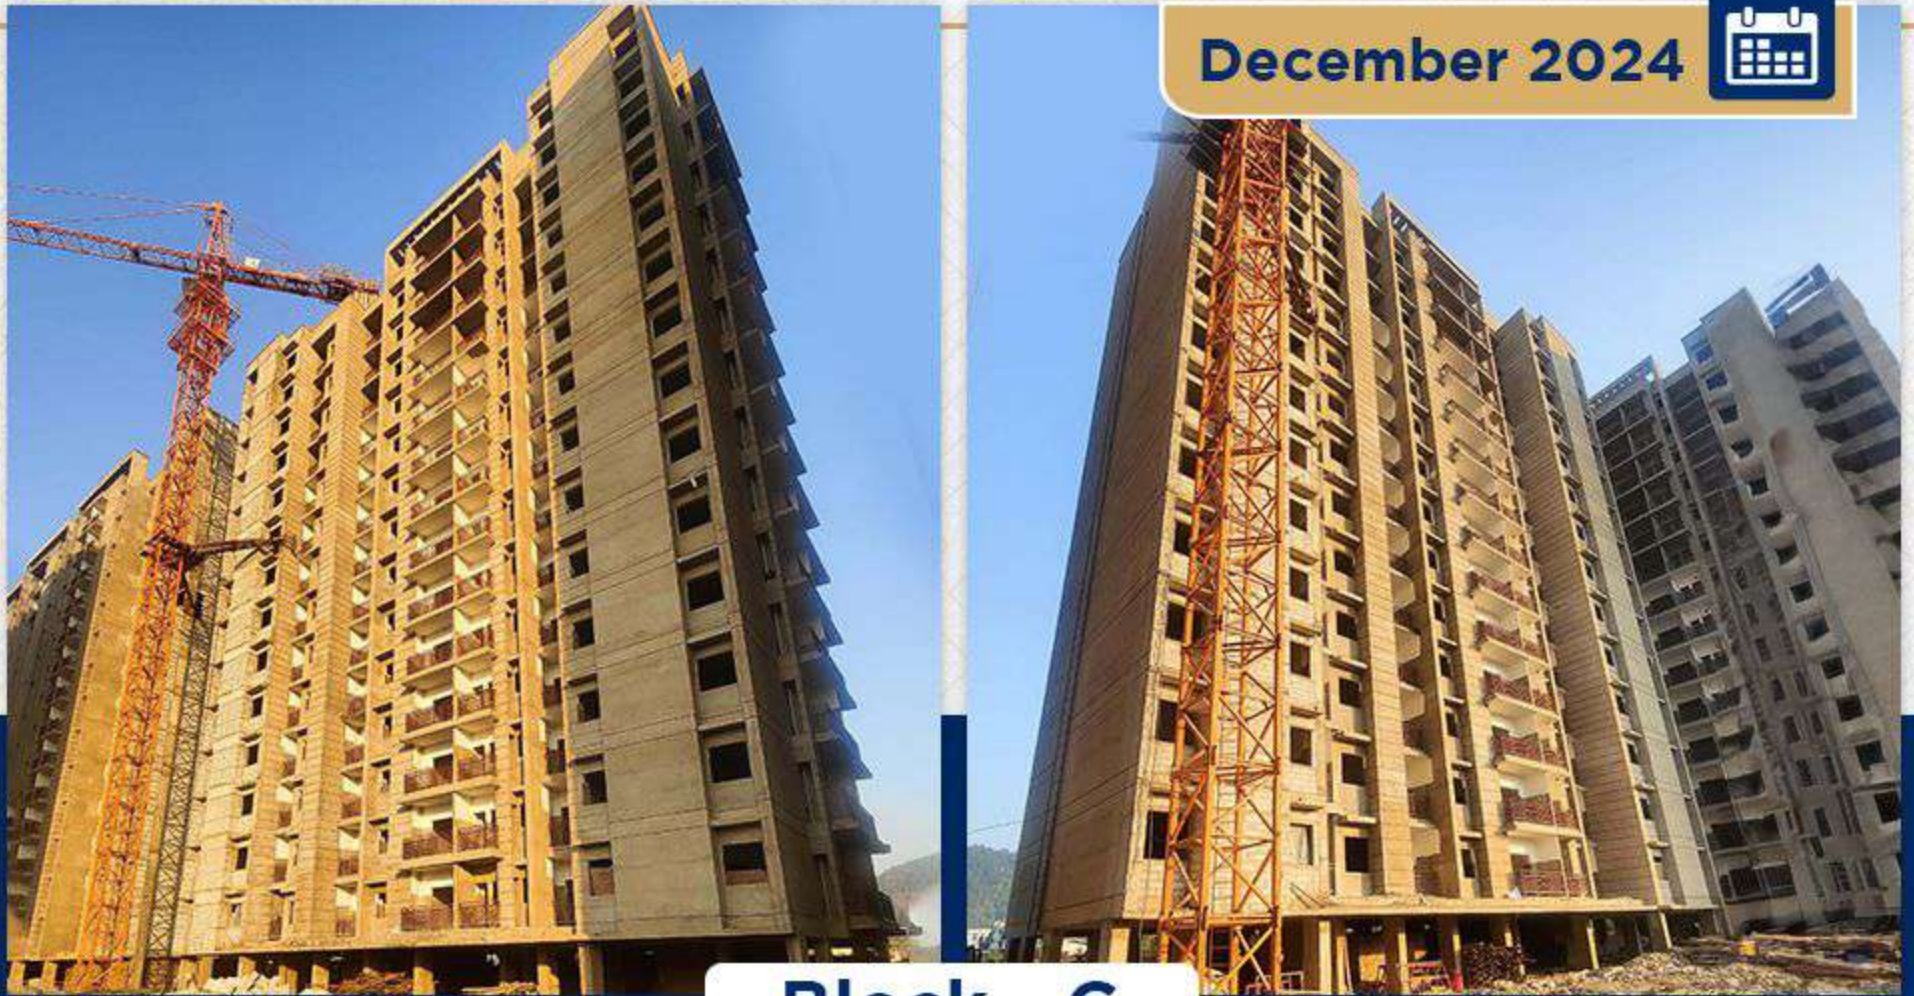

Block - C

Structural Work

- Up to 14th Floor (Terrace) roof slab casted.
- Mumty, OHWT, Pergola casted.

Plastering Work

- Up to 14th Floor internal plaster completed.
- External Plaster in Progress (95%).

Plumbing Work

- Up to 14th Floor plumbing concealed work completed.
- Vertical Sewage, Soil, Rainwater, Kitchen & Balcony outlet & Water line in progress (75%)
- Horizontal Sewage Soil line of Bathroom down slab in progress (90%)

Masonry Work

- Up to 14th Floor AAC Block masonry completed.

Internal Wall Putty Work

- Up to 9th floor internal wall putty in progress

Waterproof Work

- Up to 14th Floor down slab waterproofing in progress.


Tiles Work

- 3rd Floor, floor tiles fitting in progress.

Electrical Work

- Up to 14th Floor electrical pipe concealed work completed.

December 2024

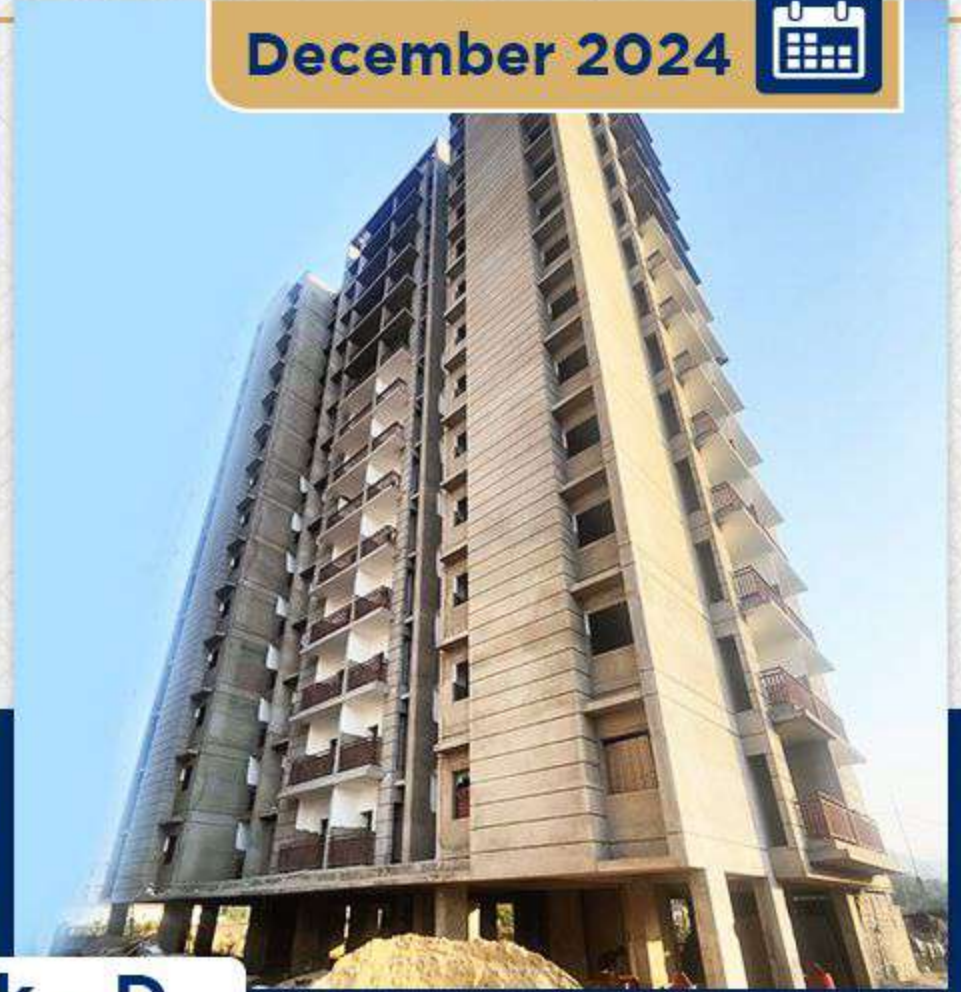

Block - D

Structural Work

- Up to 14th Floor (Terrace) roof slab casted.
- Mumty, OHWT, Pergola casted.

Plastering Work

- Up to 14th Floor internal plaster completed.
- External Plaster in Progress (90%).

Plumbing Work

- Up to 14th Floor plumbing concealed work completed.
- Vertical Sewage, Soil, Rainwater, Kitchen & Balcony outlet & Water line in progress (50%)
- Horizontal Sewage Soil line of Bathroom down slab in progress (35%)

Masonry Work

- Up to 14th Floor AAC Block masonry completed.

Internal Wall Putty Work

- Up to 8th floor internal wall putty in progress


Waterproof Work

- Up to 14th Floor down slab waterproofing is completed.

Electrical Work

- Up to 14th Floor electrical pipe concealed work completed.

December 2024

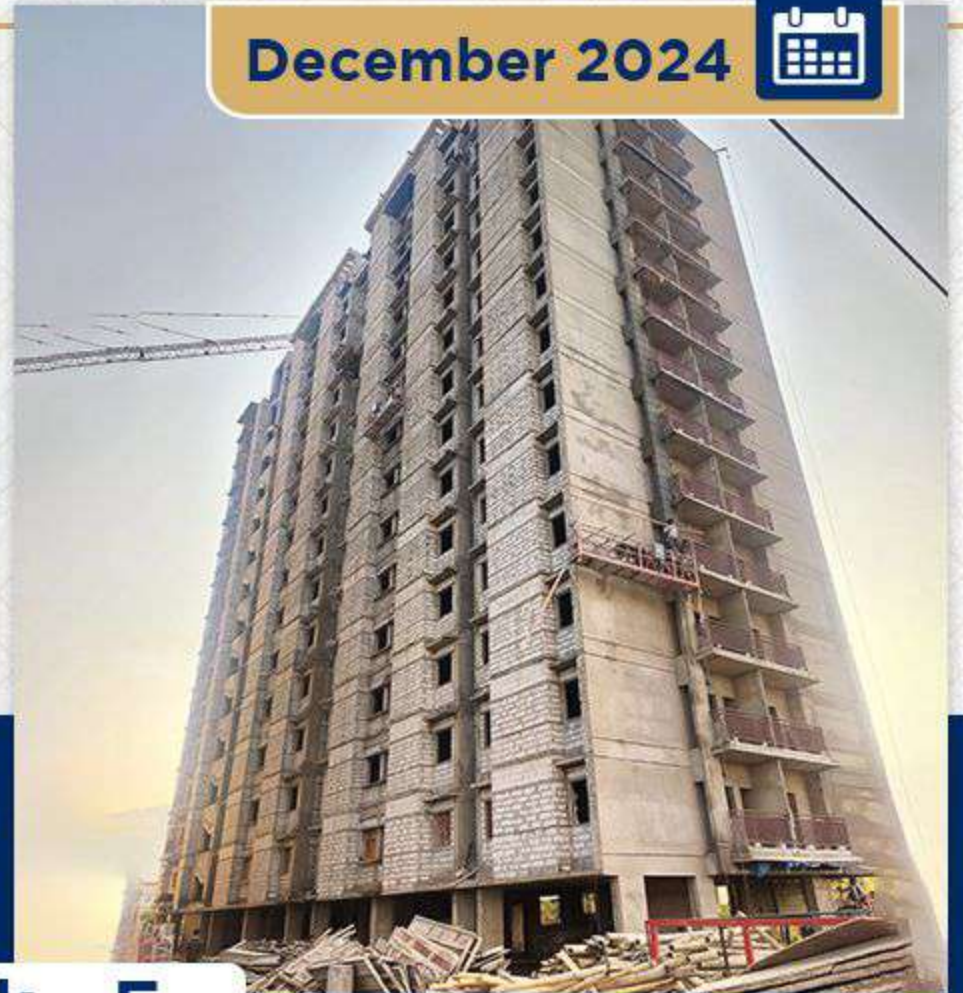

Block - E

Structural Work

- Up to 14th Floor (Terrace) roof slab casted.
- Mumty, OHWT, Pergola casted.

Plastering Work

- Up to 13th Floor internal plaster completed.
- External Plaster in Progress (10%).

Plumbing Work

- Up to 13th Floor plumbing concealed work completed.

Masonry Work

- Up to 13th Floor AAC Block masonry completed.
- 14th Floor AAC Block Masonry in progress

Internal Wall Putty Work

- Up to 8th floor internal wall putty in progress

Waterproof Work

- Up to 8th Floor down slab waterproofing in progress.

Electrical Work

- Up to 13th Floor electrical pipe concealed work completed.
